(A) Energy Management

Estimated cost saving for a 500W LED solar spot light each:-

- 0.5 kWh × RM 0.45 per kWh × 10 working hours per day × 30 days per month =

RM67.50 per LED solar spot light monthly, on average

(A) Energy Management

Update as at May26

Total Purchase Record of 500W LED Solar Spotlight as at 19.05.2026

	Project Site	Q'ty (Nos)	Saving/Light (RM)	Saving (RM)	Location
1	P187	508	67.50	34,290.00	CLQ, Site Office, Guard House, Corridor Area
2	P188				
3	P191				
4	P192				
5	P194				
6	P195				
7	P196				
8	P197				
9	P198				
10	P199				
11	P200				
12	P201				
13	P202				
14	P203				
15	P204				
16	JS Store				
Total Saving per month (RM)				**34,290.00**	

Latest update as at Sept26

Total Purchase Record of 500W LED Solar Spotlight as at 09.09.2026

	Project Site	Q'ty (Nos)	Saving/Light (RM)	Saving (RM)	Location
1	P187	639	67.50	43,132.50	CLQ, Site Office, Guard House, Corridor Area & Portable solar tower light
2	P188				
3	P191				
4	P192				
5	P194				
6	P195				
7	P196				
8	P197				
9	P198				
10	P199				
11	P200				
12	P201				
13	P202				
14	P203				
15	P204				
16	P207				
17	JS Store				
Total Saving per month (RM)				**43,132.50**	

i. Solar LED Spot Light at project site /CLQ

New project sites to compulsory implement the Solar LED Spotlight

1) P197 Se. Ruma – Done √
2) P198 Bukit Tunku – Done √
3) P199 Semenyih (Noble Gate) – Done √
4) P201 Reya (In progress) – Done √
5) P203 Broga (BirchPark) – Done √
6) P204 Broga (Eco Radiance) – Done √
7) P206 Shotlot (Eco Ardence) – to implement
8) P207 Factory (Eco Business Park 7) - – Done √
9) P208 Rosedale (Ancubic) - to implement

i. Solar LED Spot Light at project site /CLQ

P207







Modification of solar power LED spotlight for improvement （more portable）



20 sets to fabricate at store (Fabrication in progress at P201 Reya)

- To fabricate a frame to hang with 4 nos of solar LED spotlights
- Solar panels to be recharged during daytime for LED spotlights.
- The panels and wiring can plug off from spotlights for it to be used at night time.

i. Solar LED Spot Light at project site /CLQ

Portable Solar LED Tower Light



Prototype frame made by site



Bulk fabrication from JS Store



Solar LED Spotlight installation at P201 site.

i. Solar LED Spot Light at project site /CLQ

Portable Solar LED Tower Light






Solar LED Spotlight installation at P201 site.

i. Solar LED Spot Light at project site /CLQ

Portable Solar LED Tower Light



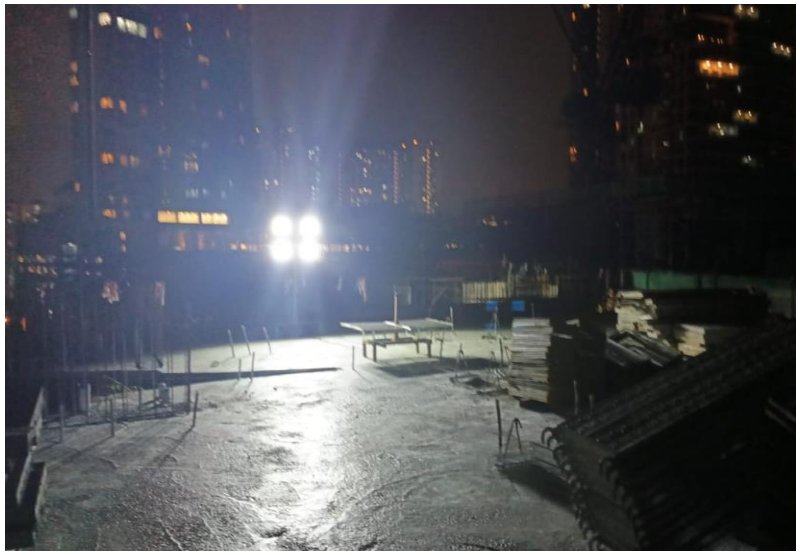






i. Solar LED Spot Light at project site /CLQ

Portable Solar LED Tower Light

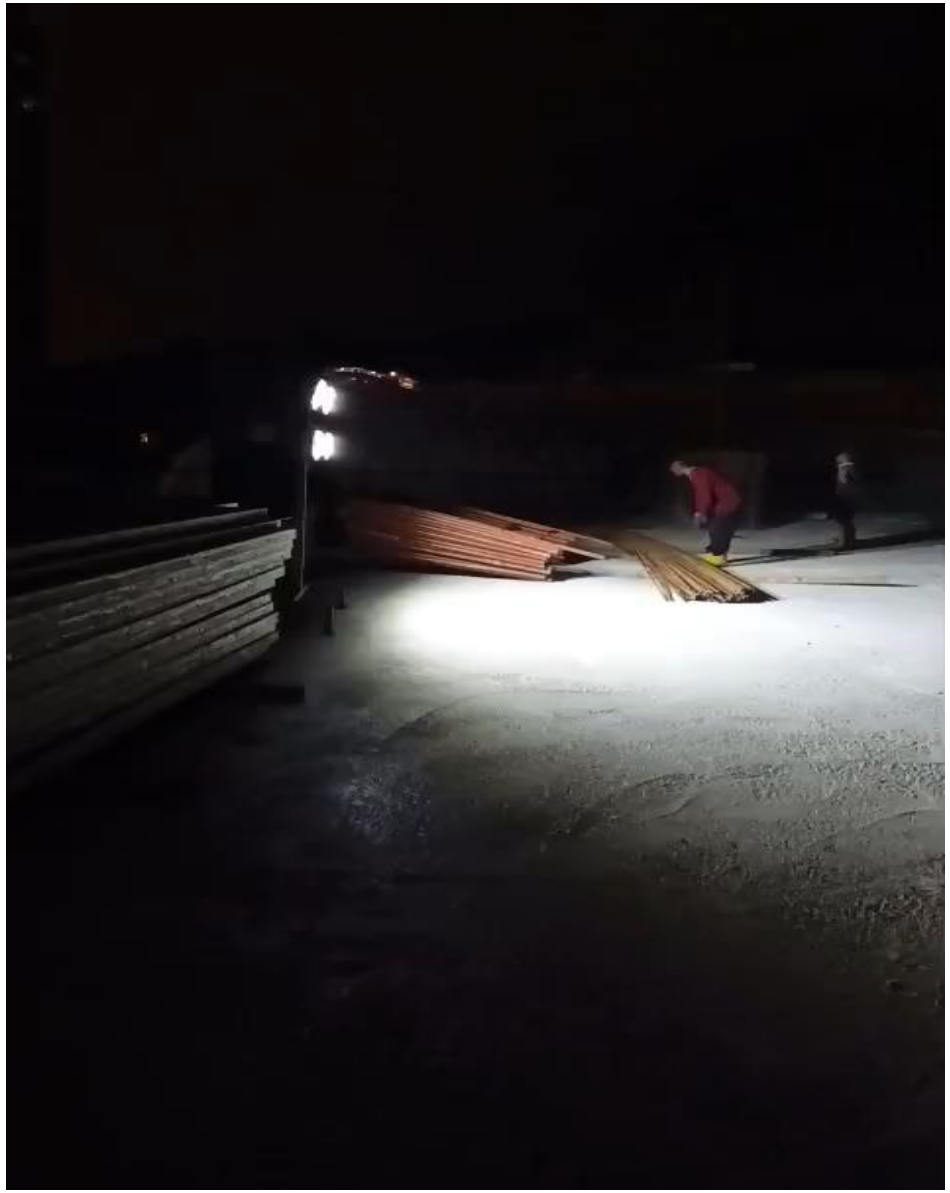

i. Solar LED Spot Light at project site /CLQ

Portable Solar LED Tower Light

Portable Solar LED Tower Light Distribution

No	Site	Qty
1	P200 Stellaris	4
2	P201 Reya	4
3	P208 Rosedale	4
4	P210 Senja	4
5	TBA	4
		20

(A) Energy Management

Battery Forklift

1) P187 Southville City and P195 Tri Ara – 2 units of 3 tonnes battery operate forklift (Brand: Lonking)

- Diesel forklift = 10 litres of diesel (8 hrs) x RM 4.80 per litre = RM 48 per day.

- Battery forklift = 80V/280Ah, efficiency of charge @90% = 24.88 kwh (for 6 hrs)

- Electricity consumption per day (24.88kwh/6 hrs x 8hrs x RM0.542/kwh) = RM18 per day.

(RM30/day or 62% of cost saving as compare with diesel usage)

Benefit: Reduce carbon emission & cost saving

(A) Energy Management

Battery Forklift





Current site using Battery (EV) forklift are:-

1) P197 Eco Sanctuary (Brand: Lonking 3.0mt)
2) P187 M Sinar Bangi (Brand: Lonking 3.0mt)
3) P192 AMIKA Subang (Brand: Zoomlion 3.5mt)
4) P193 Metropark Subang (Brand: Zoomlion 3.5mt)

Newly added:-

5) P196 Damayan Putra Heights (Brand: Lonking 3.5mt)
6) P191 Eco Ardence Maya (Brand Lonking 3.5mt) – target delivery date on 21/9/26.

(A) Energy Management

MEGABATT – CONSTRUCTION SECTOR
(BESS: Amplification Effect)

SUNRISE SHARES ENERGY
Powered by Sunrise

Most of the construction sites are facing difficulty in applying for **large incoming power** from Utilities Company (TNB). To compensate for the shortage in incoming power, the construction companies will be **using Genset** at sites which are **not environmental-friendly and expensive.**

As better alternative, MegaBatt can provide **"Amplification Effect"** to compensate for the shortage in incoming power at construction sites.

Input Current (TNB)
60A-100A
Continuous



Output Current
200A-400A
Intermittent

The MegaBatt achieves an "Amplification effect" by taking a small continuous current (from 60A-100A) from utilities, to provide a large intermittent power output (up to 400A).

(A) Energy Management

Battery Energy Storage Solution (BESS)

- P196 Putra Heights x 1 unit (In use)
- P201 Reya x 2 units (In use)
- Johan Setia Store x 1 unit (In use)



MegaBatt
(Sustainable Genset)

Advantages:-

1) No carbon emissions (using TNB power supply instead of genset)
2) No noise

- **Coming sites to use BESS:-**

1) P208 Ancubic x 2 units – Target delivery in Oct26.
2) P210 Bkt Jelutong x 2 units - Target delivery in Oct26 .
3) Proposed for Glenmarie project. - TBA

(A) Energy Management

Battery Energy Storage Solution (BESS)

P196 Putra Heights x 1 unit (Delivered)
Currently power up the following:-

1) TC x 1 no
2) PH x 2 nos
3) Placing Boom x 1 no
4) Site office & Other usage









Battery Energy Storage Solution (BESS)

P201 Reya x 1 unit (Delivered)
Currently power up the following:-

1) TC x 1 no (In use)
2) PH x 2 nos (early next year)
3) Placing Boom x 2 nos (early next year)
4) CLQ (In use)
5) Site office & Other usage (In use)





(B) Water

1) Some sites such as P185, P187, P191 & P195 have implemented rainwater harvesting system(Refer photos below).

Proposed sites to implement rainwater harvesting system:-

1) P197 Kota Kemuning (not implementing CLQ to be removed)
2) P199 Semenyih (not implementing- using tube well)
3) P200 Segambut (unable to implement-CLQ inside building)
4) P201 KL East (To be implemented once CLQ done set up)
5) P202 Cyberjaya (not implementing-using tube well)
6) P203 Broga (not implementing)
7) P207 EBP 7 - TBA
8) P208 Ancubic –TBA
9) P210 Bkt Jelutong - TBA


(B) Water

Rainwater harvesting system at P191 Eco Ardence Maya







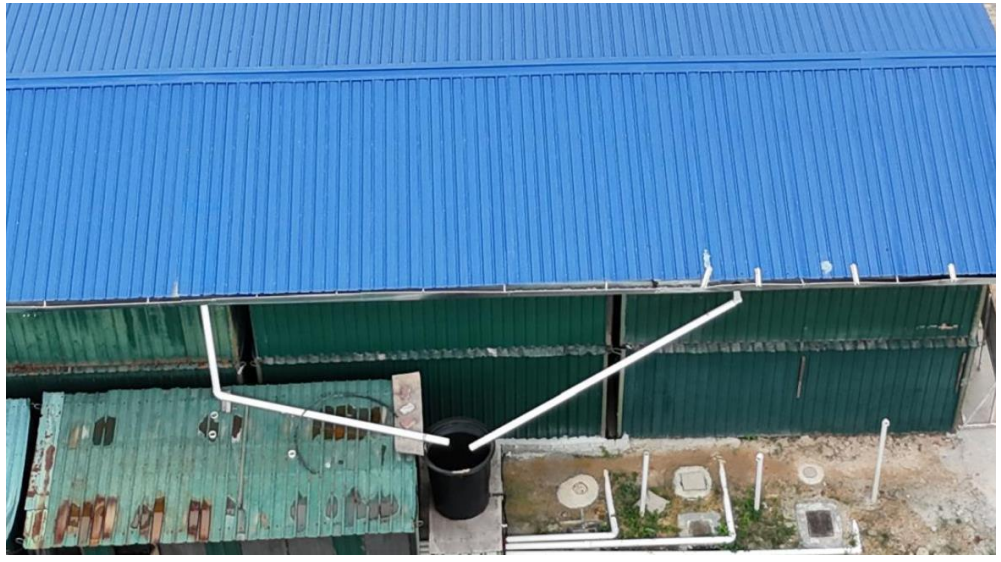

(B) Water

Rainwater harvesting system at P187 Southville







(B) Water

Sprinkler system P187 Southville



(C) Waste Management (RECYCLE PROGRAM-Waste diversion from landfill)

Benefit:

- **Reduce carbon & greenhouse gas emission (can be included in scope 1 emission for ESG reporting /disclosure)**
- **Reduce soil and water pollution**
- **Conserve natural resources**

(C) Waste Management

Timber waste sent for recycle





(C) Waste Management

Used pallet sent to recycle






(C) Waste Management

Recycle use cooking oil (P200)





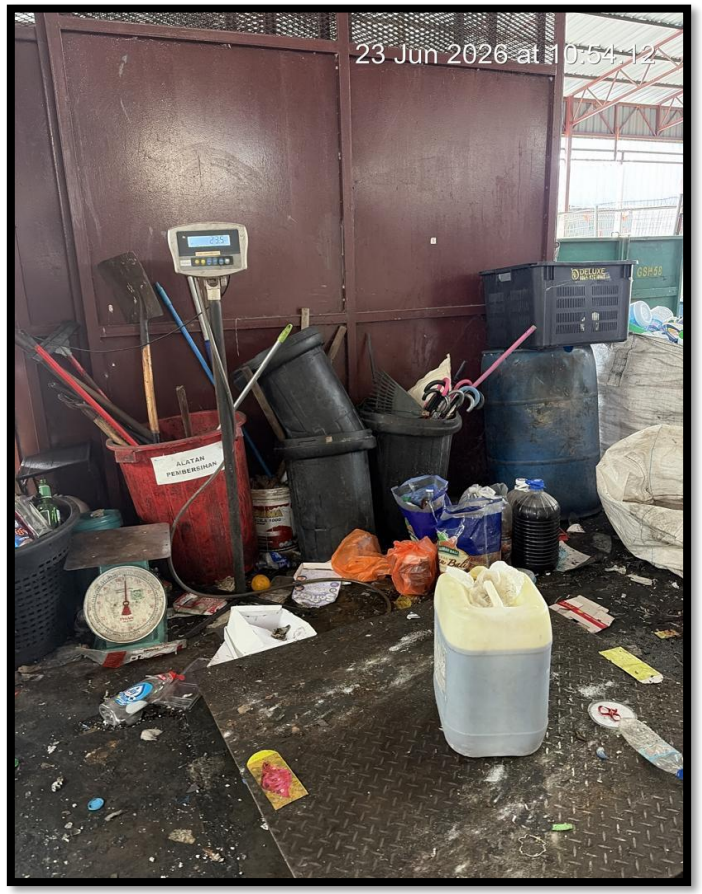

(C) Waste Management

Year 2025 Scrap by materials (All Sites)

Month	Metal (MT)	Plastic (MT)	Paper (MT)
Jan-25	63.5	-	3.85
Feb-25	90.93	-	3.69
Mar-25	57.93	-	-
Apr-25	47.97	-	2.34
May-25	61.81	1.26	2.25
Jun-25	60.36	1.46	1.89
Jul-25	80.59	-	2.16
Aug-25	94.07	-	1.35
Sep-25	234.8	-	0.32
Oct-25	125.1	-	-
Nov-25	198.76	-	-
Dec-25	147.01	0.56	0.75
Total (MT)	**1262.83**	**3.28**	**18.6**

Year 2026 Scrap by materials (All Sites)

Month	Metal (MT)	Plastic (MT)	Paper (MT)
Jan-26	135.94	-	-
Feb-26	73.82	-	3.21
Mar-26	89.14	-	2.99
Apr-26	61.49	-	4.28
May-26	58.3	-	0.94
Jun-26	49.54	-	5.71
Jul-26	66.34	-	0.7
Aug-26	36.16	1.44	2.62
Sep-26			
Oct-26			
Nov-26			
Dec-26			
Total (MT)	**570.73**	**1.44**	**20.45**
