INTA BINA GROUP BERHAD

Registration No. 201501009545 (1134880-W)

(Incorporated in Malaysia)

MINUTES OF THE ESG COMMITTEE MEETING NO. 12 ON MONDAY,21 SEPTEMBER 2026 AT 2.30 PM

Present	**Department**
Lee Yih (LY)	Contract
Ang Yee Sze (AYS)	Contract
Ling Tong Hock (LTH)	Project
Chan Weng Sang (Vincent)	Project
Muhammad Hafiz Lou Bin Abdullah (Kenneth)	M&E
Cheng Lay Ngo (Christine)	Admin
Tengku Naharudy Bin Tengku Ahmad (Rudy)	Admin
Kua Ka Cun (KKC)	Purchasing
Tee Chye Hong (Rainbow)	Purchasing
Hun Chew Yong (HCY)	Finance
Annie Chong (Annie)	Finance
Raylen Laran Larrobis (Raylan)	QAQC
Muhamad Hafizudin Bin Agus Salim (MH)	Safety
Zuraidah Binti Musbah	EO

Absent with apologies	
Lee Wen Si (LWS)	Project
Mohamad Afiq Bin Suhaimi	M&E
Lee Kam Weng (LKW)	Finance
Siti Narissa Binti Nazri (SN)	QAQC
Muhammad Hudzaifah Bin Shakirin (MHS)	Safety
Mohd Noor Fitri Bin Idris (MN)	Safety
Muhammad Zuhairi Azhar Bin Zaherman (MZ)	Safety
Nurul Zulainie Binti Zulkefli	EO
Tan Pei Ting	ISO

Directors by invitation

Paul Lim

1.0 Confirmation of minutes

1.1 The committee members reviewed the minutes of the previous Meeting held on 12 June 2026. There being no comments and amendments, the minutes were unanimously confirmed by the members and signed by LY as a correct record of the proceedings.

2.0 Minutes of minutes

2.1 Initiatives:
1) Anti corruption – To prioritise and disclose
2) Community/Society – To disclose only
3) Diversity – To disclose only
4) Energy Management – To prioritise and disclose
5) Health and safety – To prioritise and disclose
6) Labour practices and standards – To disclose only
7) Supply chain management – To disclose only
8) Data Privacy – To prioritise and disclose
9) Water – To prioritise and disclose
10) Waste management – To prioritise and disclose
11) Emission – To prioritise and disclose
12) Economic performance – To disclose only
13) Training and development – To prioritise and disclose
14) Forced/compulsory labour – To disclose only

2.2 Initiatives which are highlighted in red is on-going now.

3.0 Action plans

Group 1 Member – KKC, Rainbow, Vincent, MN, Kenneth, CYL

3.1 Group 1 reported the following progress of the action plans.

(A) Energy management

i. Introduce and installation of **solar spotlight** at project site / CLQ

- Adoption of 500W Solar LED Spotlights across sites
- Group 1 presented that the estimated cost saving per number of LED solar spotlight (operating 10 hours/day at RM 0.45/kWh) at RM 67.50 monthly, on average
- Total cost saving contributed by LED solar spotlight is updated as below,

Total Purchase Record of 500W LED Solar Spotlight as at 09.09.2026

	Project Site	Q'ty (Nos)	Saving/Light (RM)	Saving (RM)	Location
1	P187				
2	P188				
3	P191				
4	P192				
5	P194				
6	P195				
7	P196				CLQ, Site Office, Guard House, Corridor Area & Portable solar tower light
8	P197				
9	P198	639	67.50	43,132.50	
10	P199				
11	P200				
12	P201				
13	P202				
14	P203				
15	P204				
16	P207				
17	JS Store				
Total Saving per month (RM)				**43,132.50**	

Total cost saving contributed by LED solar spotlight is **Rm43,132.50**
updated by 9th September 2026

- Mr Paul requested to compare on cost saving of solar spotlight and conventional spotlight

- Adopted the consultant's guidance under the Bursa CSI framework to use Construction Floor Area (CFA) instead of contract sum as the basis for measuring electricity saving intensity, to ensure a more accurate ESG performance measurement.

- Group 1 presented that P197, P198, P199, P201, P203, P204, P207 are using solar LED spot light tower at site / CLQ, and upcoming will implement at P206 and P208.

- Group 1 presented that previously the solar frame are unstable, so now there are improvement by fabricate the standardise frame at store, there are 20 sets to fabricate at store, to distribute 4 units each to P200, P201, P208, P210

- Solar panels to be recharged during daytime for LED spotlights, so the panels and wiring can plug off from spotlights for it to be used at night time.



Prototype frame





Solar LED Spotlight installation at P201 site.

- Site claimed that there are enough lighting for site to work at night using solar LED spot light tower





Site using solar lighting at night

ii. **Battery Forklift**

- Group 1 reported that two unit of 3 tonnes battery forklift has been deployed to P187 and P195

1. Diesel Forklift
   - **Fuel Consumption:** 10 litres per 8-hour shift
   - **Diesel Rate:** RM 4.80 per litre
   - **Daily Cost:** $10\ \text{L} \times \text{RM}\ 4.80 = \text{RM}\ \mathbf{48.00}\ /\ \text{day}$

2. Battery Electric Forklift
   - **Battery Capacity:** $80\text{V} \times 280\text{Ah} = 22,400\ \text{Wh} = \mathbf{22.4}\ \text{kWh}$
   - **Charge Required (@ 90% efficiency):** $22.4\ \text{kWh} \div 0.90 = \mathbf{24.89}\ \text{kWh}$ (for 6 hours of operation)
   - **Energy Required for 8-hour shift:** $(24.89\ \text{kWh} \div 6\ \text{hrs}) \times 8\ \text{hrs} = \mathbf{33.18}\ \text{kWh}$
   - **Electricity Tariff Rate:** RM 0.542 per kWh
   - **Daily Cost:** $33.18\ \text{kWh} \times \text{RM}\ 0.542 = \text{RM}\ \mathbf{17.99} \approx \text{RM}\ \mathbf{18.00}\ /\ \text{day}$

- Total cost saving RM30/day or 62% compare with diesel usage
- Current site using is P197, P187, P192 & P193, upcoming site to use is P191 & P196

iii. **Battery Energy Storage Systems (BESS)**

- Group 1 reported that BESS is being used at site P196, P201 & Johan Setia Store
- 1 no. of BESS at P196 is powering up 1 tower crane, 2 passenger hoist, 1 placing boom, site office and other usage
- 1 no. of BESS at P201 is powering up 1 tower crane, CLQ, site office and other usage

<u>(B) Water Management</u>

i. Use **rainwater harvesting** at CLQ and site office.

- Group 1 presented that P185, P187, P191 & P195 have implemented rainwater harvesting system
- Local authorities charge RM 0.07 per m^3 for ground/rainwater extraction
- Discussed regulatory issues regarding authorities enforcing multi-metering and double-charging across collection tanks. The committee agreed to request to waive the installation costs while maintaining statutory compliance
- LY to bring the matter up to MBAM for discussion.

<u>(C) Waste Management</u>

i. **Material Recycling & Waste Minimisation**

- Currently sites are recycling the waste concrete to make it into concrete slab and concrete blocks
- Timber waste, used pallet being sent for recycle at every construction site.
- Construction sites have implemented the recycling of used cooking oil.



Timber waste



Used pallet



Used cooking oil

Year 2026 Scrap by materials (All Sites)

Month	Metal (MT)	Plastic (MT)	Paper (MT)
Jan-26	135.94	-	-
Feb-26	73.82	-	3.21
Mar-26	89.14	-	2.99
Apr-26	61.49	-	4.28
May-26	58.3	-	0.94
Jun-26	49.54	-	5.71
Jul-26	66.34	-	0.7
Aug-26	36.16	1.44	2.62
Sep-26			
Oct-26			
Nov-26			
Dec-26			
Total (MT)	**570.73**	**1.44**	**20.45**

Total scrap by material for Year 2026.

Group 2 – Member – YCS, LTH, MZ, Raylan, SN

3.2 Group 2 reported the following progress of the action plans.

(A) Social

i. **Driver Training on weight regulations and proper loading procedures**

- Regular health screening for drivers
  - To propose to HR every year (now we have 6 full time drivers +1 adhoc)

ii. **Proposed enhancing CSR through donations to schools, annual donations and should be included in ESG reporting.**

iii. Proposed to launch a formal ESG Recycling Awareness Campaign to promote recycling practices and enhance ESG awareness across the organisation.

Item No.	Description	Recycle time	Recycling Purpose
1	WBP (Weather and Boil Proof) Plywood - 7ply	3-4 times	Formwork
2	Tego Plywood - 5 ply	4-5 times	Formwork
3	Floor gard protection	3 times (last at carpark)	Protection
4	Excess Concrete	-	Road barrier , Spacer block, PC slab
5	Corner Bead (small pieces)	-	Protection angle at tile drop to prevent chipping and damage.
6	Reuse Damaged Scaffold		Fabricate filing racks, storage racks and other items. (workers quarters bed frame, cabinet)

- **WBP Plywood / Formwork:** LTH highlighted that the plywood/formwork can be reused up to 2 - 3 times before deterioration occurs due to weather exposure.
- **Tego Plywood:** LTH highlighted that the plywood/formwork can be reused up to 3 - 4 times before deterioration occurs due to weather exposure.
- **Floor Guard:** Proven reusable up to 3 times after cleaning and proper storage.
- **Excess Concrete Reuse:** Poured into precast road barriers, spacer blocks and pc slab, most useful will be pc slab, can be used at access, reducing the steel plates. LY suggest to put in monthly progress report, so every site can update and can collect data from that.
- **Corner Bead:** Reused as edge protectors during tiling to prevent edge chipping.
- **Damage Scaffolding:** Repurposed damaged 900mm scaffold frames into cooking tables, bed frame for worker quarters.

<u>Example of recycling concrete wastage</u>

P201 PC Slab


(1)



PC Slab from Concrete Waste

Created: Mon, 2/9/2026

(2)

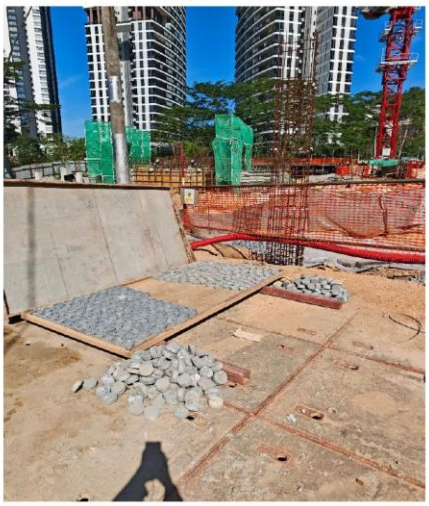

Concrete Spacer from Concrete Waste

Created: Wed, 2/11/2026

P192 Road barriers and slabs




iv. Up-skilling and Re-skilling Workers/Staffs

- Recorded over 4,000 total training man-hours last year
- Refining HR records to categorize training into **Upskilling** (supervisors taking specialized technical courses, to enahnce and advance current capabilities) and **Reskilling** (mandated role changes, such as site leaders qualifying as lifting supervisors)

v. Prposed Community & CSR Programme

- School outreach, blood donation, community clean-up tree planting, charity & festive community support programme (recent got contribution to surau).

vi. Proposed Awareness on Health & Wellbeing Programme

- Health Screening
- Mental Wellness
- Fitness & active lifestle
- Ergonomic Awareness
- Employee Assistance

All activities shall be proper recorded, quarterly review and annual reporting under ESG and IMS performance review.

Group 3 Member – LY, AYS, Christine, Rudy, MH, MHS

3.3 Group 3 reported the following progress of the action plans.

(A) Anti-Corruption

- Group 3 reported that the new joiners (up to June 2026) have completed physical training in 19 June 2026 for half day session. There are 2 sessions and each group will be 20 pax.

- Group 3 presented the Anti-Corruption training as below,

Employee Category	Training Session	Proposed Method
Senior Management	Every year	TBC
Management	Every 2 year	TBC
Executive	Every 2 year	Online
Non-Executive	Every 3 year	Online

- Christine presented that the training for senior management is conducted annually in physical session.
- Christine requested the feedback from all to complete the awareness questionnaire, the form will be shared after the meeting.
- To finalised the draft of the 20-question online awareness questionnaire for distribution to both Executive and Non-Executive level staffs.

4.0 To review and discuss the draft Sustainability Policy.

Key comments from Mr Paul:

- ESG Policy Categorisation: Suggested that the Company's ESG Policy be structured into 3 key categories: Environmental, Social and Governance.
- Environmental: To cover climate change, carbon footprint, Scope 1, Scope 2 and Scope 3 emissions, energy and water consumption/wastage.
- Social: To cover health, safety and well-being, as well as fostering a quality culture of "doing it right the first time and every time."
- Governance: To cover Anti-Bribery and Corruption (ABC) and other relevant governance practices.
- Overall Sustainability Culture: The policy should align with the Company's culture of "Better Me, Better Inta Bina, Better Malaysia", with emphasis on sustainability and continuous improvement through the adoption of appropriate technology and machinery.

5.0 To brainstorm and discuss potential improvements

- LY presented that the biodiversity score from 0.0 to 3.0, which have a good improvement.
- While for the environmental supply chain and social supply chain maintain 0.0.
- To address the zero scores under the supply chain categories, Mr Kua was tasked with drafting a 4–5 question ESG self-declaration form for suppliers and subcontractors.
- Key compliance criteria will cover no child labour, legal employment/work permits, and non-discrimination
- The form will be formally registered under the company's SOP and distributed during monthly meeting to let everyone notice on this.

6.0 Other matter

- **CSR –** Committee member proposed that we shall resume gotong-royong at the surrounding of our HQ office.
- **SOP** – Each ESG Working Group shall submit its core SOP in point form before the next meeting. The drafts will then be forwarded to Mr Chin, the SOP guideline person-in-charge, for formalisation in accordance with the Company's standard SOP templates.

- **Sustainability Awareness ("Better Malaysia"):** LY presented to the Committee on the importance of individual purchasing choices in promoting sustainability and contributing to the mitigation of environmental issues, including haze arising from regional open burning. Members were encouraged to consider purchasing consumer products carrying recognised sustainability certifications, such as RSPO-certified, FSC, PEFC and Rainforest Alliance labels.
- **Committee Member Recognition:** Suggested introducing incentives or recognition for active committee members
- **Green Financing**: Mr Paul suggested that HCY explore green financing opportunities, including financing facilities that may offer preferential interest rates upon meeting specified ESG criteria or sustainability requirements.

7.0 Date of next meeting

7.1 The date for next ESG meeting was scheduled at 8th January 2027, 10.30am.

Conclusion of meeting
The meeting concluded at 4.30pm

Signed as correct record



Lee Yih
Dated : 21st September 2026
